chart for starlight foundation plate schedule of activities 29th-nov-2017

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
0		**chart for starlight foundation plate schedule of activities 29th-nov-2017**	**10 days?**	**Sun 12/3/17**	**Fri 12/15/17**	
1		MGKB team members relocate to kiboga	0.38 days	Sun 12/3/17	Sun 12/3/17	
2		Procuring sand and transportation to site	1.5 days	Mon 12/4/17	Tue 12/5/17	1
3		aggregate procurement and transportation to site	1 day	Tue 12/5/17	Tue 12/5/17	2
4		Reinforcement steel, DPC, and BRC procurement and transportation to site	1 day	Tue 12/5/17	Tue 12/5/17	2
5		procurement of concrete mixers and vibrator	3 days	Mon 12/4/17	Wed 12/6/17	1
6		mobilisation of helpers and masons	3 days	Tue 12/5/17	Thu 12/7/17	4
7		mobilisation of site tools , procurement of timber formwork and prop plus transportation to sites	1 day	Wed 12/6/17	Wed 12/6/17	4,3
8			1 day?	Thu 12/7/17	Thu 12/7/17	
9		setting out for foundation strips and excuvation	1 day	Thu 12/7/17	Thu 12/7/17	7
10		procuring for cement and transportation to site	2 days	Thu 12/7/17	Fri 12/8/17	7
11		Anti termite treatement	1 day	Fri 12/8/17	Fri 12/8/17	9

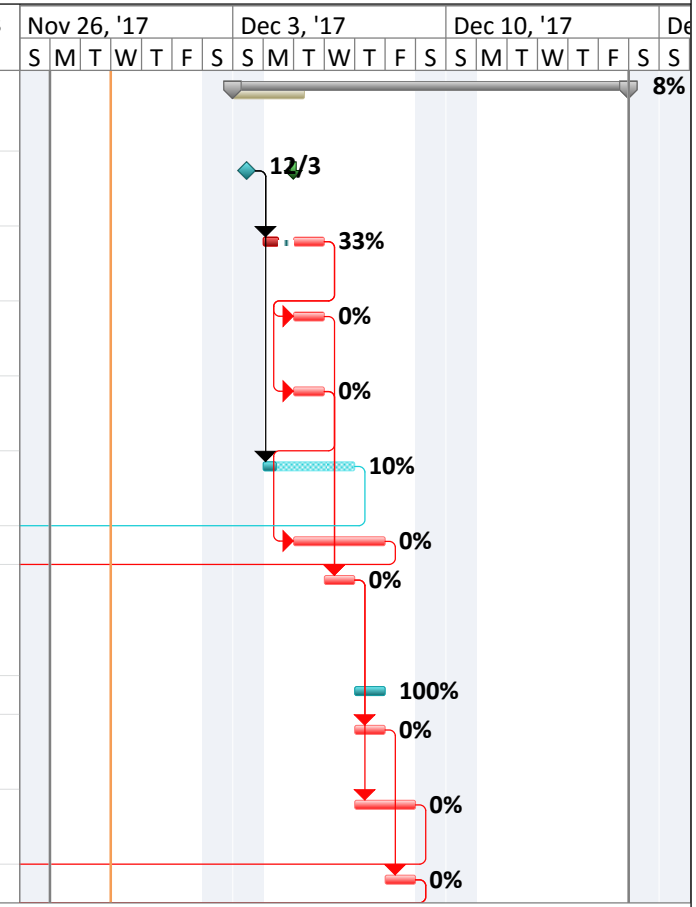

Critical	Finish-only	Manual Summary
Critical Split	Duration-only	Project Summary
Critical Progress	Baseline	External Tasks
Task	Baseline Split	External Milestone
Split	Baseline Milestone	Inactive Task
Task Progress	Milestone	Inactive Milestone
Manual Task	Summary Progress	Inactive Summary
Start-only	Summary	Deadline

chart for starlight foundation plate schedule of activities 29th-nov-2017

ID	Task Mode	Task Name	Duratio	Start	Finish	Predecessors
12		concrete blinding into foundation strips	1 day	Fri 12/8/17	Fri 12/8/17	11,10,6
13		**formwork erection and bar bending**	**1 day**	**Sat 12/9/17**	**Sat 12/9/17**	**12**
14		transportation of concrete mixer, vibrator and poker	1 day?	Sun 12/10/17	Sun 12/10/17	11,5
15		casting concrete into foundation strips	1 day	Mon 12/11/17	Mon 12/11/17	14
16		stone topping	1 day	Tue 12/12/17	Tue 12/12/1	15
17		slab concreting	1 day	Wed 12/13/17	Wed 12/13/	16
18		curing concrete	3 days	Wed 12/13/17	Fri 12/15/17	15
19		transporting back concrete mixer, vibrator and poker	1 day	Wed 12/13/17	Wed 12/13/17	17
20		dismantling form work	1 day?	Fri 12/15/17	Fri 12/15/17	18,17,19

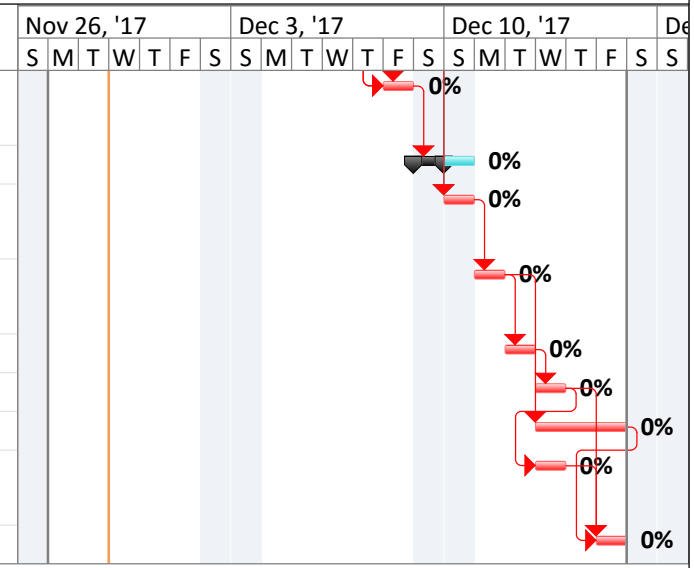

Critical	Finish-only	Manual Summary
Critical Split	Duration-only	Project Summary
Critical Progress	Baseline	External Tasks
Task	Baseline Split	External Milestone
Split	Baseline Milestone	Inactive Task
Task Progress	Milestone	Inactive Milestone
Manual Task	Summary Progress	Inactive Summary
Start-only	Summary	Deadline
